



WEEKLY PROJECT STATUS UPDATE

Project Name:	BASALT MIDDLE SCHOOL RENOVATIONS
Site Address:	51 School St. Basalt, CO
Date:	Jan. 27, 2017
TAB Associates/NV5 H+L Arch./RFSD	James McDonough, Ray Scott, Jennifer Ellsperman
FCI Project Manager:	Marc Litzen
Project Summary:	Basalt Middle School Renovation Additions, Electrical and security upgrades Site work
Key Tasks Completed This Reporting Period:	<ul style="list-style-type: none"> - Demo of drywall ceilings auditorium. - Continued demo in Media area. - Hallway ceiling tiles removed for further investigation. - MEP Demo in Auditorium started. - Temp shoring/separation wall E130 getting built.
Key Tasks for next reporting Period:	<ul style="list-style-type: none"> - New openings cut in and lintels installed. - New clouds getting framed. - New fire sprinkler lines getting installed. - Shoring wall nearing completion. - MEP rough in started throughout.
Site Conditions:	Snow, Partly cloudy toward end of week, cold. -7
Days Lost This Reporting Period:	0
Total Days Lost:	0

WEEKLY PROJECT STATUS UPDATE

Demo of drywall ceilings in Auditorium.



Continued Demo in Media area.




More Hallway ceiling tiles removed for MEP coordination.




WEEKLY PROJECT STATUS UPDATE

MEP demo in Auditorium started.

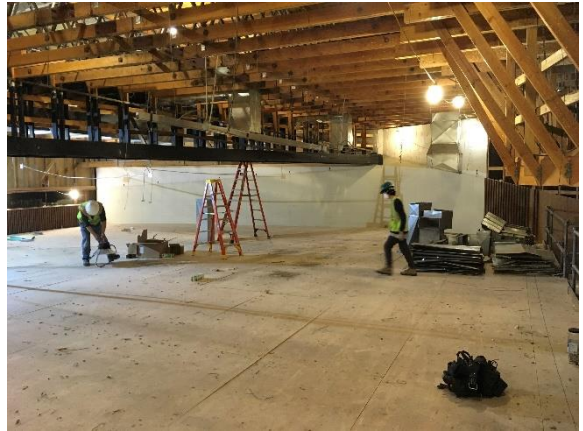

Temp shoring/separation wall started in E130, (toddler space).

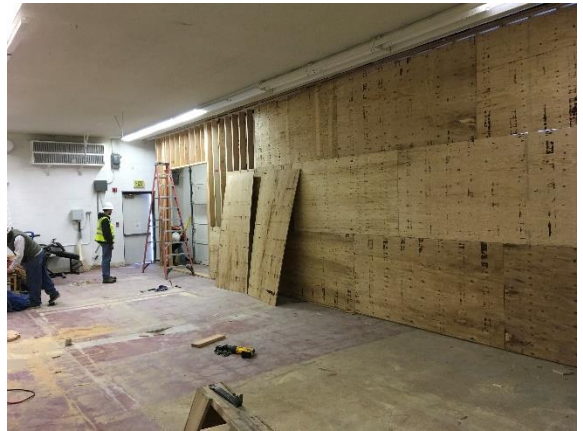

New fire sprinkler install started.

