



WEEKLY PROJECT STATUS UPDATE

Project Name:	BASALT MIDDLE SCHOOL RENOVATIONS
Site Address:	51 School St. Basalt, CO
Date:	Feb. 17, 2017
TAB Associates/NV5 H+L Arch./RFSD	James McDonough, Ray Scott, Jennifer Ellsperman
FCI Project Manager:	Marc Litzen
Project Summary:	Basalt Middle School Renovation Additions, Electrical and security upgrades Site work
Key Tasks Completed This Reporting Period:	<ul style="list-style-type: none"> - New framing in the media area. - Sound clouds in Auditorium hung. - Structure painting in auditorium completed. - MEP rough in continuing through out. - Duct work in Auditorium getting installed.
Key Tasks for next reporting Period:	<ul style="list-style-type: none"> - MEP rough in near complete in Media & Auditorium - Fire sprinkler piping in gym and Aux gym near complete - Foundation excavation started at new Aux. gym - New construction entrance established - Prep for new fire lane road started.
Site Conditions:	Partly cloudy toward end of week. Clear, spring like.
Days Lost This Reporting Period:	0
Total Days Lost:	0

WEEKLY PROJECT STATUS UPDATE


New framing in media area.



All sound clouds installed in auditorium/finishing drywall.



Structure painting in auditorium completed.

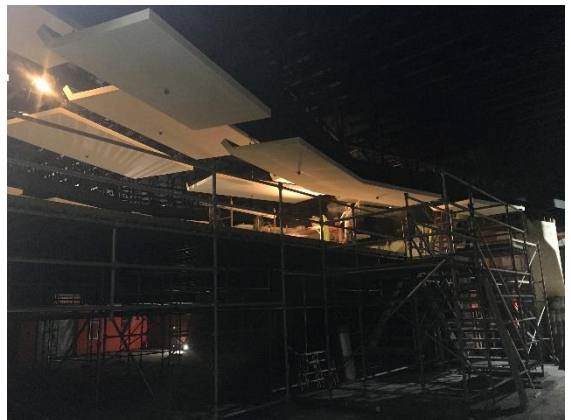

WEEKLY PROJECT STATUS UPDATE

MEP rough in continuing in Media area.



MEP rough in Auditorium, Mechanical ductwork.



MEP re-routing in Hallway for new high ceilings nearing completion.

