



WEEKLY PROJECT STATUS UPDATE


Project Name:	BASALT MIDDLE SCHOOL RENOVATIONS
Site Address:	51 School St. Basalt, CO
Date:	Feb. 24, 2017
TAB Associates/NV5 H+L Arch./RFSD	James McDonough, Ray Scott, Jennifer Ellsperman
FCI Project Manager:	Marc Litzen
Project Summary:	Basalt Middle School Renovation Additions, Electrical and security upgrades Site work
Key Tasks Completed This Reporting Period:	<ul style="list-style-type: none"> - MEP rough in near complete in Media & Auditorium - Fire sprinkler piping in gym and Aux gym near complete - Foundation excavation started at new Aux. gym - New construction entrance established - Prep for new fire lane road started.
Key Tasks for next reporting Period:	<ul style="list-style-type: none"> - Cut in new return air location in auditorium. - Drywall fur out on upper auditorium walls started. - Footer concrete at aux gym poured. - New water line to fire Hydrant on North side going in. - Fire lane road dirt base started.
Site Conditions:	Partly cloudy toward end of week. Clear, spring like.
Days Lost This Reporting Period:	0
Total Days Lost:	0

WEEKLY PROJECT STATUS UPDATE

MEP rough in near complete in Media & Auditorium.



Fire sprinkler piping in gym and Aux gym near complete.

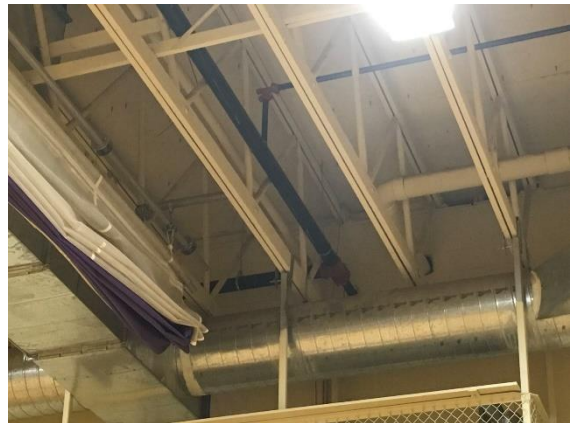

Foundation excavation started at new Aux. gym.



WEEKLY PROJECT STATUS UPDATE

New construction entrance established.



Prep for new fire lane road started.



Trench for underground electrical at sound booth in auditorium.

