




## WEEKLY PROJECT STATUS UPDATE

<b>Project Name:</b>	<b>BASALT MIDDLE SCHOOL RENOVATIONS</b>
Site Address:	51 School St. Basalt, CO
Date:	March 10, 2017
TAB Associates/NV5 H+L Arch./RFSD	James McDonough, Ray Scott, Jennifer Ellsperman
FCI Project Manager:	Marc Litzen
Project Summary:	Basalt Middle School Renovation Additions, Electrical and security upgrades Site work
Key Tasks Completed This Reporting Period:	<ul style="list-style-type: none"> <li>- Cut in new return air location in auditorium.</li> <li>- Drywall Started hanging on Media area walls.</li> <li>- Foundation backfilled at movement space.</li> <li>- New water line to fire Hydrant on North side completed.</li> <li>- Underground plumbing at new bathroom in movement.</li> </ul>
Key Tasks for next reporting Period:	<ul style="list-style-type: none"> <li>- Slab pour at addition to movement.</li> <li>- Drywall finishing started at Media area walls.</li> <li>- MEP rough in completed in auditorium.</li> <li>- New football field access for kids established.</li> <li>- Soffit work exterior classrooms started.</li> </ul>
Site Conditions:	Partly cloudy toward end of week. Snow Monday
Days Lost This Reporting Period:	0
Total Days Lost:	0

WEEKLY PROJECT STATUS UPDATE

Cut in return air duct in CMU auditorium.

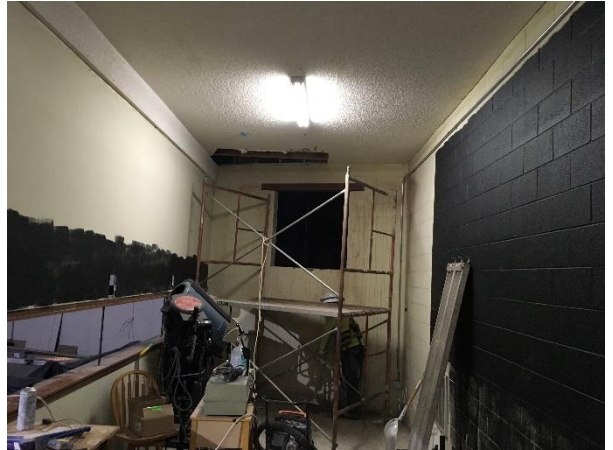

Drywall hanging started in the Media area.



Foundations back filled at the New Movement and foundation drain installed at addition.




WEEKLY PROJECT STATUS UPDATE

New Waterline to fire Hydrant completed.



Underground plumbing for new bathroom and fixtures in movement area completed.

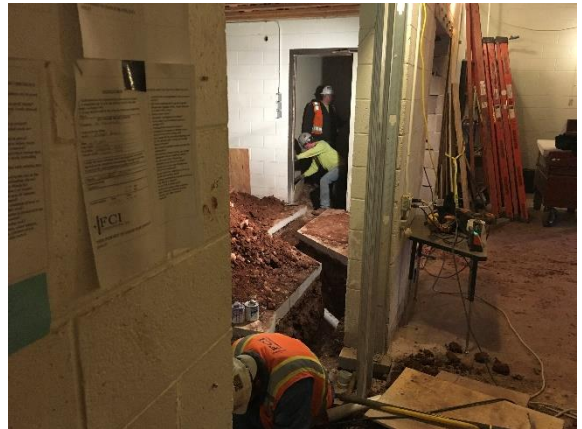

New Drywell installed next to new fire lane road.

