



WEEKLY PROJECT STATUS UPDATE

Project Name:	BASALT MIDDLE SCHOOL RENOVATIONS
Site Address:	51 School St. Basalt, CO
Date:	April 14, 2017
TAB Associates/NV5 H+L Arch./RFSD	James McDonough, Ray Scott, Jennifer Ellsperman
FCI Project Manager:	Marc Litzen
Project Summary:	Basalt Middle School Renovation Additions, Electrical and security upgrades Site work
Key Tasks Completed This Reporting Period:	<ul style="list-style-type: none"> - Grid and MEP rough in Media & computer area. - Classroom addition slab pour completed. - Auditorium stage progress. - Site concrete started in prep for asphalt. - Movement addition structural sheeting completed.
Key Tasks for next reporting Period:	<ul style="list-style-type: none"> - Auditorium stage front Poured back - Sound baffles installed in auditorium. - Curb and gutter pours for asphalt. - Bleacher pad concrete poured. - Music room structure painting.
Site Conditions:	Partly cloudy little moisture toward end of week.
Days Lost This Reporting Period:	0
Total Days Lost:	0

WEEKLY PROJECT STATUS UPDATE


Grid and MEP rough in computer media area



Classroom addition slab poured.



Auditorium stage progress.

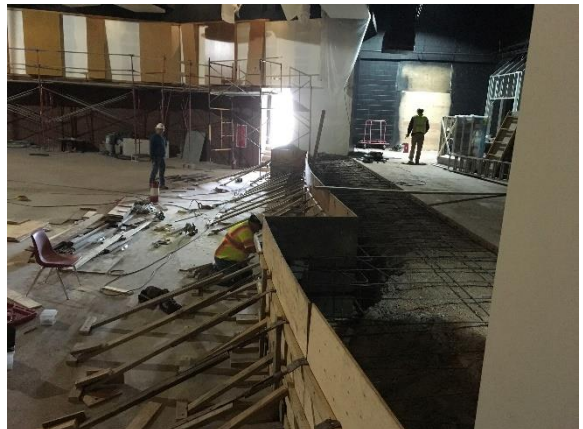

WEEKLY PROJECT STATUS UPDATE

Site concrete started, Curb and Gutter.



Movement addition shear sheeting install.



Football bleacher pad rebar and prep.

