



WEEKLY PROJECT STATUS UPDATE

Project Name:	BASALT MIDDLE SCHOOL RENOVATIONS
Site Address:	51 School St. Basalt, CO
Date:	April 7, 2017
TAB Associates/NV5 H+L Arch./RFSD	James McDonough, Ray Scott, Jennifer Ellsperman
FCI Project Manager:	Marc Litzen
Project Summary:	Basalt Middle School Renovation Additions, Electrical and security upgrades Site work
Key Tasks Completed This Reporting Period:	<ul style="list-style-type: none"> - Playground area grading continuing. - Stage demo and forming for new. - New lintels and opening in Music room. - Painting the Media room. - Classroom addition prep for Slab.
Key Tasks for next reporting Period:	<ul style="list-style-type: none"> - Grid and MEP rough in Media & computer area. - Classroom addition slab pour completed. - Auditorium stage pours completed. - Site concrete started in prep for asphalt. - Movement addition structural sheeting completed.
Site Conditions:	Partly cloudy little moisture toward end of week.
Days Lost This Reporting Period:	0
Total Days Lost:	0

WEEKLY PROJECT STATUS UPDATE


Playground grading continuing and underground utilizes being rerouted.



Stage demo and forming for new getting ready.



New lintels and openings in music room started.

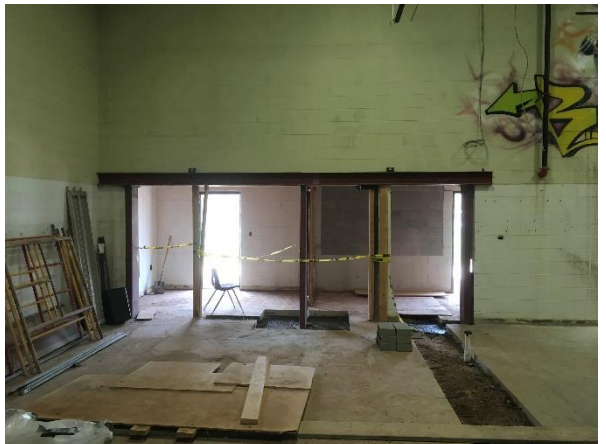

WEEKLY PROJECT STATUS UPDATE

Painting the media/computer started.



Classroom addition slab prep and footers completed.



Football bleacher pad prep.

