



## WEEKLY PROJECT STATUS UPDATE

|   |  |
|---|--|
| <b>Project Name:</b>                          | <b>BASALT MIDDLE SCHOOL RENOVATIONS</b>  |
| Site Address:                                 | 51 School St. Basalt, CO   |
| Date:   | April 7, 2017  |
| TAB Associates/NV5<br>H+L Arch./RFSD          | James McDonough, Ray Scott, Jennifer Ellsperman  |
| FCI Project Manager:                          | Marc Litzen  |
| Project Summary:                              | Basalt Middle School Renovation<br>Additions, Electrical and security upgrades<br>Site work  |
| Key Tasks Completed<br>This Reporting Period: | <ul style="list-style-type: none"> <li>- Playground area grading continuing.</li> <li>- Stage demo and forming for new.</li> <li>- New lintels and opening in Music room.</li> <li>- Painting the Media room.</li> <li>- Classroom addition prep for Slab.</li> </ul>  |
| Key Tasks for next<br>reporting Period:       | <ul style="list-style-type: none"> <li>- Grid and MEP rough in Media &amp; computer area.</li> <li>- Classroom addition slab pour completed.</li> <li>- Auditorium stage pours completed.</li> <li>- Site concrete started in prep for asphalt.</li> <li>- Movement addition structural sheeting completed.</li> </ul> |
| Site Conditions:                              | Partly cloudy little moisture toward end of week.  |
| Days Lost This<br>Reporting Period:           | 0  |
| Total Days Lost:                              | 0  |

## WEEKLY PROJECT STATUS UPDATE


Playground grading continuing and underground utilizes being rerouted.



Stage demo and forming for new getting ready.



New lintels and openings in music room started.

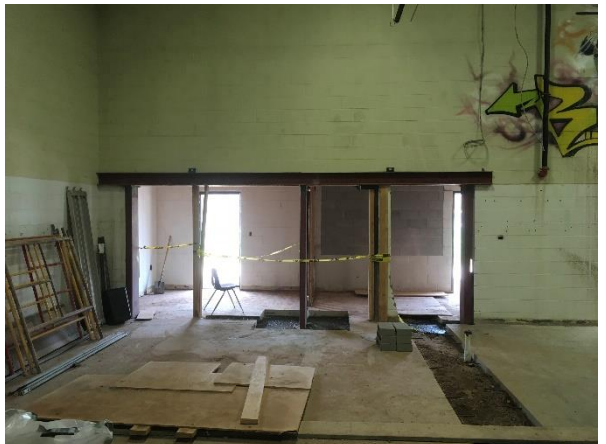

WEEKLY PROJECT STATUS UPDATE

Painting the media/computer started.



Classroom addition slab prep and footers completed.



Football bleacher pad prep.

